



## FLORIDA DEPARTMENT OF TRANSPORTATION - DISTRICT FOUR


### A1A Improvements Project in Hollywood

A1A from Sheridan Street to Monroe Street

Financial Project ID Numbers: 432323-1-52-01

#### MONTHLY PROJECT UPDATE AND UPCOMING ACTIVITIES

The Graph below depicts the project's status of completion in green, while the blue depicts anticipated progress of completion in the month of May.

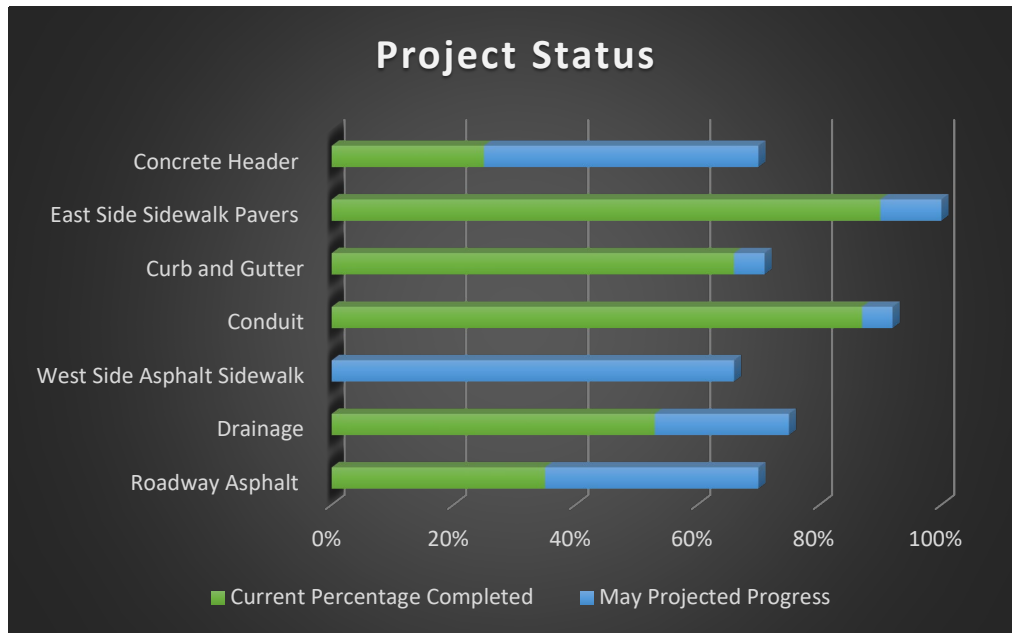

#### BI-WEEKLY SCHEDULE OF ACTIVITIES

##### April 29 – May 13:

- Concrete header installation at various locations between Sheridan Street and Nevada Street
- East side sidewalk paver installation at various locations between Arizona Street and Johnson Street
- Curb and gutter installation at various locations between Sheridan Street to Nevada Street
- Conduit installation at various locations between Sheridan Street to Nevada Street
- Drainage installation at various locations between Sheridan Street to Nevada Street

##### May 13 – May 27

- Concrete header installation at various locations between Nevada Street and Johnson Street
- East side sidewalk paver installation at various locations between Johnson Street and Connecticut Street
- Asphalt Sidewalk installation at various locations between Sheridan Street and Johnson Street
- Drainage installation at various locations between Nevada Street and Johnson Street
- Roadway asphalt between Sheridan Street and Johnson Street

*\*Locations are subject to change at the contractor's discretion\**

#### CONTACT INFORMATION

Heidy Cuevas, P.E.— Construction Project Manager

Phone: (954) 958-7653

Email: [Heidy.Cuevas@dot.state.fl.us](mailto:Heidy.Cuevas@dot.state.fl.us)

Rebecca Guerrero— Community Outreach Specialist

Phone: 954-940-7605

Email: [rguerrero@corradino.com](mailto:rguerrero@corradino.com)

Construction Cost: \$9,366,292.09

Construction Start Date: October 9, 2017

Anticipated Completion: Summer 2019
