



## FLORIDA DEPARTMENT OF TRANSPORTATION - DISTRICT FOUR


### A1A Improvements Project in Hollywood

A1A from Sheridan Street to Monroe Street

Financial Project ID Numbers: 432323-1-52-01

#### MONTHLY PROJECT UPDATE AND UPCOMING ACTIVITIES

The Graph below depicts the project's status of completion in green, while the blue depicts anticipated progress of completion in the month of June.

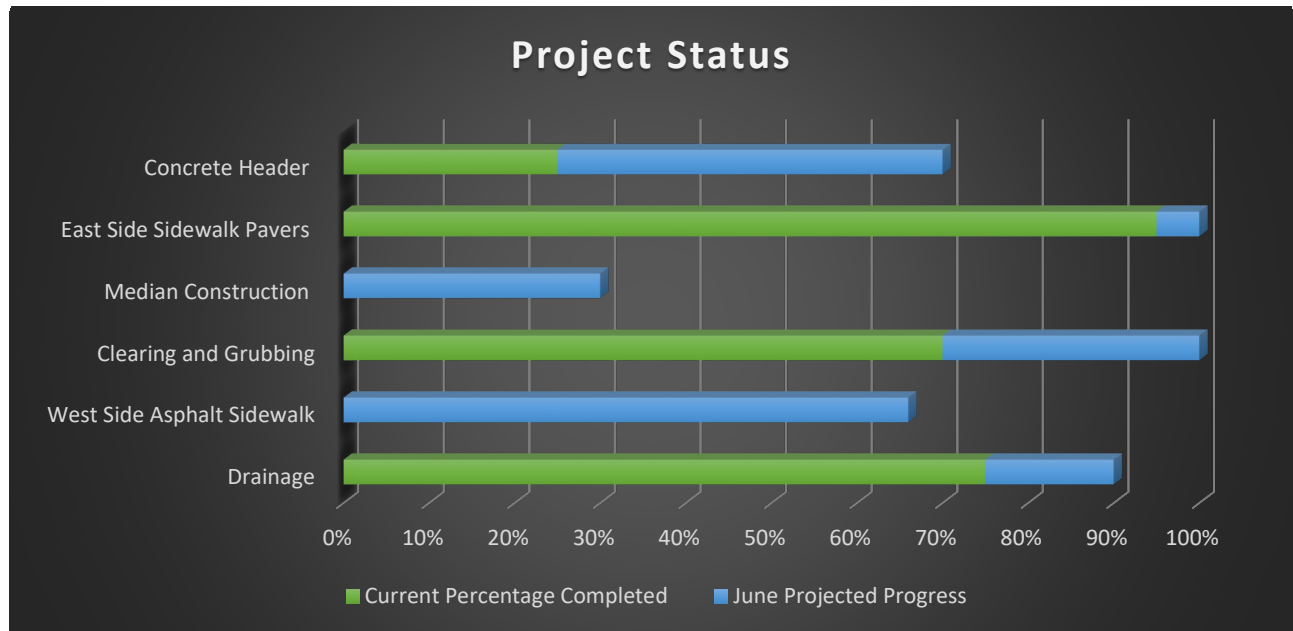

#### BI-WEEKLY SCHEDULE OF ACTIVITIES

##### June 3 – June 17:

- Concrete header installation at various locations between Nevada Street and Johnson Street.
- East side sidewalk paver punch list items at various locations between Arizona Street and Johnson Street.
- Curb and gutter installation at various locations between Nevada Street and Johnson Street.
- Asphalt sidewalk installation at various locations between Sheridan Street and Johnson Street.

##### June 17– June 30

- East side sidewalk paver punch list items at various locations between Johnson Street and Connecticut Street.
- Drainage installation at various locations between Johnson Street and Arizona Street.
- Clearing and grubbing between Johnson Street and Arizona Street.
- Median construction between Sheridan Street and Nevada Street.

*\*Locations are subject to change at the contractor's discretion\**

#### CONTACT INFORMATION

Heidy Cuevas, P.E.— Construction Project Manager

Phone: (954) 958-7653

Email: heidy.cuevas@dot.state.fl.us

Rebecca Guerrero— Community Outreach Specialist

Phone: 954-940-7605

Email: rguerrero@corradino.com

#### FLORIDA DEPARTMENT OF TRANSPORTATION MISSION STATEMENT

The Department will provide a safe transportation system that ensures the mobility of people and goods, enhances economic prosperity, and preserves the quality of our environment and communities.

Construction Cost: \$9,366,292.09

Construction Start Date: October 9, 2017

Anticipated Completion: Summer 2019
