


FLORIDA DEPARTMENT OF TRANSPORTATION - DISTRICT FOUR

A1A Improvements Project in Hollywood

A1A from Sheridan Street to Monroe Street Financial Project ID Number: 432323-1-52-01

MONTHLY PROJECT UPDATE AND UPCOMING ACTIVITIES

The Graph below depicts the project's major activities. The green is the percent completed to date, while the blue depicts anticipated production for the month of November.

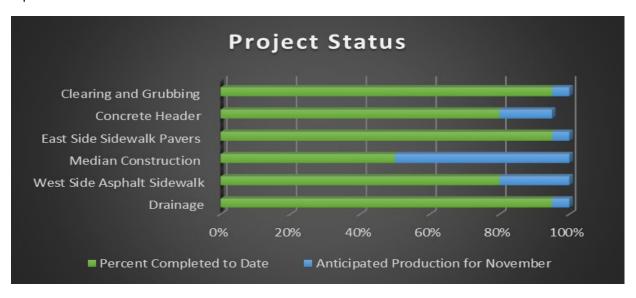

BI-WEEKLY SCHEDULE OF ACTIVITIES *Weather Permitting*

November 1st - November 15th

- Drainage installation at various locations between Arizona Street and Johnson Street
- Concrete header installation at various locations between Arizona Street and Johnson Street
- Median construction between Johnson Street and Garfield Street
- Sidewalk base material on the west side of the road between Hollywood Boulevard and Johnson Street
- · Electrical conduit installation at various locations between Johnson Street and Sheridan Street
- Sidewalk and driveway construction between Arizona Street and Johnson Street

November 16th – **November 29**th *Construction activities will be suspended in observance of the Thanksgiving Holiday, Thursday, November 28 through Sunday, December 1. *

- Asphalt sidewalk installation between Arizona Street and Johnson Street
- Median construction between Hollywood Boulevard and Johnson Street
- Electrical conduit installation at various locations between Sheridan Street and Johnson Street
- Asphalt paving operation between Monroe Street and Hollywood Boulevard

CONTACT INFORMATION

Heidy Cuevas, P.E.— Construction Project Manager

Phone: 954-958-7653

Email: heidy.cuevas@dot.state.fl.us

Rebecca Guerrero — Community Outreach Specialist

Phone: 954-940-7605

Email: rguerrero@corradino.com

FLORIDA DEPARTMENT OF TRANSPORTATION MISSION STATEMENT

The Department will provide a safe transportation system that ensures the mobility of people and goods, enhances economic prosperity, and preserves the quality of our environment and communities.

Construction Cost: \$9,366,292.09 Construction Start Date: October 9, 2017 Anticipated Completion: Winter 2020

^{*}Locations are subject to change at the contractor's discretion*
