



CONSTRUCTION UPDATE: SR 7 FROM SW 25TH STREET TO FILLMORE STREET IN HOLLYWOOD, MIRAMAR, AND WEST PARK

Project Overview

- **CONTRACT TIME:** Project is on time. Originally 1100 contract days, adjusted to 1189 to include weather and holidays (68% complete)
- **PROJECT TIMELINE:** January 2015 - Summer 2018
- **COST:** Project is on budget. Originally \$30.7 million, adjusted to \$29.8 million including \$900K in Cost Saving Initiatives. Approximately \$19.7 million paid to date (66% complete)
- **PONDS:** 8 ponds located in project limits, Construction on ponds is 80% completed

Project Timeline *These dates are subject to change due to weather and other unforeseen conditions

- **Phase 5 - Northbound Widening - Completed on time on January 19, 2017**
- **Phase 6 - Southbound Reconstruction - Completion expected in October 2017**
 - Segment A: North of Washington Street to Fillmore Street (incl. Hollywood Boulevard): Nearly Complete, except for signal by others at West Hollywood Shopping Plaza and related connection
 - Segment B: From Pembroke Road to North of Washington Street - Approximately 50% complete
 - Segment C: North of Hallandale Beach Boulevard to Pembroke Road—Approximately 50% complete
- **Phases 7 & 8 - Completion expected in Spring 2018**
 - Constructing/Finishing medians, paving all lanes final layer of asphalt, and finish signing and pavement markings


Traffic Impact

- One lane in each direction of SR 7 / US 441 from Hallandale Beach Boulevard/Miramar Parkway to Fillmore Street will be closed intermittently Monday through Friday between 9 a.m. and 4 p.m. and Monday through Friday between 9 p.m. and 6 a.m. through the end of the project.
- Southbound traffic is shifted west along SR 7/US 441 from south of Fillmore Street to 1000' south of Hollywood Boulevard. Northbound traffic will remain on the east side allowing for a work zone in the center of the roadway to construct raised medians.
- Traffic is shifted east along SR 7/US 441 from SW 26th Street to 1000' south of Hollywood Boulevard in order to reconstruct the west side of the road. Two lanes of traffic in each direction will be maintained.

November 2016



April 2017

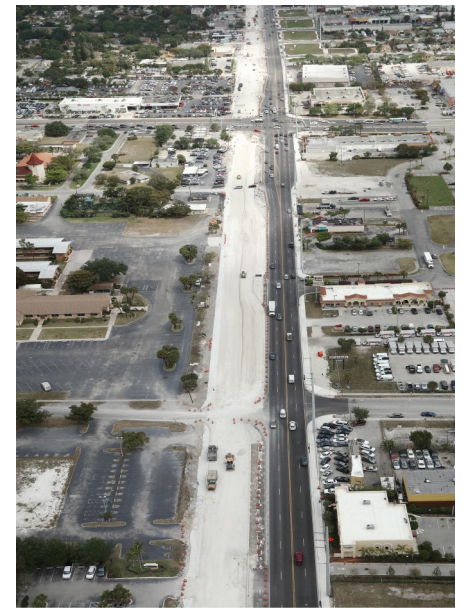

Project Updates

If you would like to receive project updates, lane closure information, as well as a weekly traffic report distributed by FDOT, please email ddiaz@corradino.com the subject of “SR 7 from SW 25th Street to Fillmore Street in Hollywood, Miramar, and West Park”. Public participation is solicited without regard to race, color, national origin, age, sex, religion, disability or family status.

Flyer updated May 12, 2017

For Additional Project Information

Contact Mrs. Dayana Diaz, Community Outreach Specialist
Phone: (954) 940-7585 | Email: ddiaz@corradino.com

www.fdot.gov
Innovative, Efficient, Exceptional
